

**NORTH COUNTY CORRIDOR
EXPRESSWAY TRANSPORTATION AUTHORITY**


ITEM: 7a

SUBJECT: NCC Project Schedule Update

STAFF RECOMMENDATIONS: Information Only

FISCAL IMPACT: None with this item

ID	Task Name	Duration	Start	Finish	% Complete	Predecessors	2008				2009				2010				2011				2012				2013			
							Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4
61	Engineering and Land Net Surveys - Route Adoption	163 days	Sat 9/27/08	Mon 5/11/09	72%																									
66	Task 4 - Environmental Scoping of Alternatives Identified for Studies - Route Adoption	151.8 days	Fri 10/3/08	Fri 5/1/09	89%																									
72	Task 5 - General Environmental Studies - Route Adoption	200 days	Mon 10/13/08	Fri 7/17/09	71%																									
125	Task 6 - Draft Environmental Document - Route Adoption	149 days	Tue 2/24/09	Mon 9/21/09	41%																									
139	Task 7 - Circulate Draft Env Doc and Select Preferred Project Alternative- Route Adoption	34 days	Fri 7/17/09	Wed 9/2/09	0%																									
151	Task 8 - Prepare and Approve Project Report and Final Program EIR - Route Adoption	118 days	Thu 5/14/09	Mon 10/26/09	0%																									
170																														
171	APPROVAL OF CEQA PROGRAM EIR AND ROUTE ADOPTION BY CTC - Must complete by Dec 2009	43 days	Fri 10/9/09	Wed 12/9/09	0%																									
172	Submit request to District for Decemeber CTC action	0 days	Fri 10/16/09	Fri 10/16/09	0%																									
173	District submits CTC request to HQ Division of Design	0 days	Fri 10/16/09	Fri 10/16/09	0%	172																								
174	Route Adoption Map	5 days	Fri 10/9/09	Fri 10/16/09	0%	172FF																								
175	HQ Division of Design submits CTC request to HQ Programming	0 days	Mon 10/26/09	Mon 10/26/09	0%																									
176	HQ Programming finalizes CTC Agenda language for Nov 2009 Mtg	0 days	Mon 11/9/09	Mon 11/9/09	0%																									
177	Division of Design finalizes CTC Book Item for Dec 2009 CTC Mtg	0 days	Mon 11/16/09	Mon 11/16/09	0%																									
178	Submits to HQ CTC Liaison Office	0 days	Mon 11/16/09	Mon 11/16/09	0%																									
179	CTC Approval	0 days	Wed 12/9/09	Wed 12/9/09	0%																									
180	CTC APPROVAL OF ITIP PROGRAMMING IN THE 2010 STIP - Must complete by April 2010	0 days	Tue 4/13/10	Tue 4/13/10	0%	171FS+90 days																								
181																														
182	TIER I EIR/EIS HYBRID ENV. DOC. FOR CORRIDOR AND 1st PHASE OF CONSTRUCTION	1049 days	Mon 7/14/08	Tue 7/17/12	0%																									
270	BEGIN SUPPLEMENTAL TIER II ENV DOCS FOR PHASES 2, 3, 4 AND 5	1 day	Tue 12/21/10	Tue 12/21/10	0%	269																								

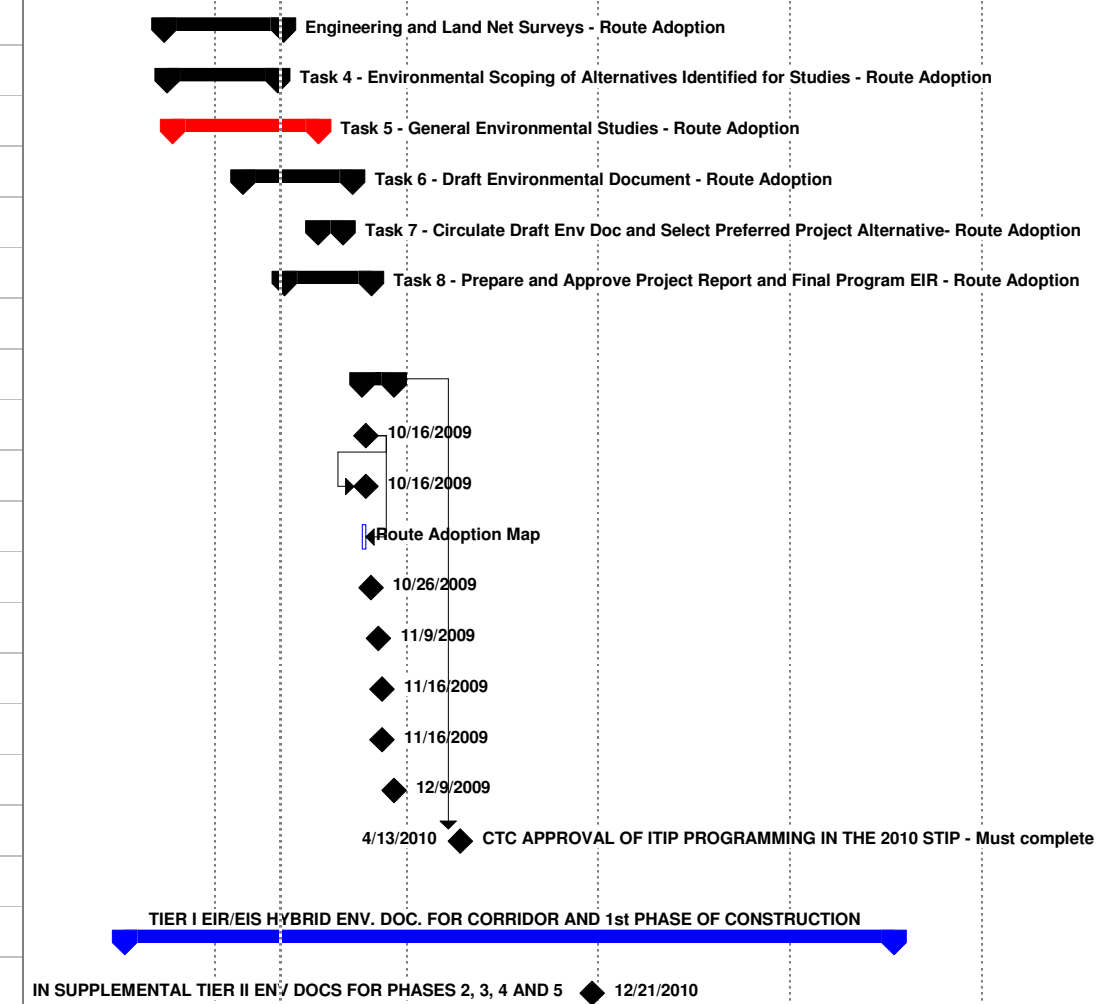

NORTH COUNTY CORRIDOR
 Hammett Rd IC at State Route 99
 to SR 108/120 East of Oakdale

Task		Progress		Summary		Rolled Up Critical Task		Rolled Up Progress		External Tasks		Group By Summary	
Critical Task		Milestone		Rolled Up Task		Rolled Up Milestone		Split		Project Summary			

- 4 **ROUTE ADOPTION - PROGRAMATIC EIR (CEQA)**
Scott Smith
Gail Miller
- 20 **Updated Project Information (Previous Studies and Reports)**
Antone (559) 243-8181
- 27 **Traffic Studies - Route Adoption**
Assumptions:
99 Connection Points
CT Biggest concerns:
impacts to 00
8 lanes-99
Must document that
- 72 **Task 5 - General Environmental Studies - Route Adoption**
Technical Studies done in mid April
