



County of Stanislaus
Department of Public Works
1716 Morgan Rd.
Modesto, CA. 95358
Phone (209) 525-4130

Measure L

County Name: **Stanislaus County**

Project Name and Number: Crows Landing Rd Bridge @ SJ River-Seismic II (9589)

Date: 6/30/2026

Revenue		Expenses	
County Funds		Project Budget	\$1,403,921.83
Federal Funds	\$0.00	Encumbered	
State Funds		Expended - Measure L	\$102,650.83
Measure L Funds BUDGETED	\$102,650.83	Available - Measure L	\$0.00
Other Funds - SB1	\$1,301,271.00		
Total	\$1,403,921.83		

Estimated Completion Date: Project is Complete

Phase: Project is Complete

PAGE 2: Crows Landing Rd Bridge @ SJ River (Seismic II)

Overall Project Details:

The project entails replacement of a structurally deficient bridge with a new bridge designed to current structural and geometric standards. The replacement bridge will improve safety, resiliency, and capacity within that corridor of Crows Landing Road.

Project Status:

Project is complete, currently closing out project with contractor

Add photos/renderings:



County of Stanislaus
Department of Public Works
1716 Morgan Rd.
Modesto, CA. 95358
Phone (209) 525-4130

Measure L

County Name: **Stanislaus County**

Project Name and Number: Golden State/Golf/Berkeley (HUTA) 9605(055064)

Date: 6/30/2026

Revenue		Expenses	
TURLOCK	\$173,414.00	Project Budget	\$8,593,311.00
Federal Funds	\$6,992,018.00	Encumbered	
State Funds		Expended - Measure L	\$526,967.63
Measure L Funds	\$807,254.00	Available - Measure L	\$280,286.37
Other Funds - SB1	\$620,625.00		
Total	\$8,593,311.00		

Estimated Completion Date: 10/31/2026

Phase: CONSTRUCTION

Overall Project Details:

The project location currently lacks essential features such as turn lanes, proper drainage, adequate visibility, pedestrian access, and ADA compliance. Project plans include installing traffic signals coordinated with Union Pacific Railroad to reduce congestion and enhance safety.

Project Status:

County's electrical contractor working on electrical infrastructure at the Railroad Crossing.

Add photos/renderings:



County of Stanislaus
Department of Public Works
1716 Morgan Rd.
Modesto, CA. 95358
Phone (209) 525-4130

Measure L

County Name: **Stanislaus County**

Project Name and Number: Sidewalk Project (200002, 200003, 200004, 200005, 200006)

Date: 6/30/2026

Revenue		Expenses	
County Funds		Project Budget	\$5,348,772.47
Federal Funds		Encumbered	
State Funds	\$0.00	Expended - Measure L	\$327,201.70
Measure L Funds	\$4,048,772.47	Available - Measure L	\$3,721,570.77
Other Funds-BCIF	\$1,300,000.00		
Total	\$5,348,772.47		

Estimated Completion Date: 2028

Phase: Construction (CON)

Overall Project Details:

Install new sidewalks at four different areas within the County. To include Airport neighborhood area, Bret Harte School area, Robertson Rd Elementary School area, and Denair area.

Project Status:

Airport (200002) Construction of the project is complete, and the Project Completion and Final Delivery reports have been prepared by the County and accepted by Caltrans. Therefore, the project is now officially closed out.

Bret Harte (200003) Construction of the project is complete, and the Project Completion and Final Delivery reports have been prepared by the County and accepted by Caltrans. Therefore, the project is now officially closed out.

Robertson (200004) The project will be going to the October 2026 CTC meeting for allocation of construction funds. The project is on track to start construction in late spring or early summer 2027.

Downtown Denair (200005) The project is working towards environmental clearance and completing the needed utility exploration to finalize the geometric layout.

Turlock (200006) Retention released and cashed by Contractor. Project is 100% Complete.

PROJECT 200002 -200006; Add photos/renderings:



County of Stanislaus
Department of Public Works
1716 Morgan Rd.
Modesto, CA. 95358
Phone (209) 525-4130

Measure L

County Name: **Stanislaus County**

Project Name and Number: **Peletized Asphalt Rubber Overlay Test Sections (220013)**

Date: **6/30/2026**

Revenue		Expenses	
County Funds		Project Budget	\$275,000.00
Federal Funds		Encumbered	
State Funds		Expended - Measure L	\$117,293.72
Measure L Funds BUDGETED	\$275,000.00	Available - Measure L	\$157,706.28
Other Funds - Cal cycle	\$0.00		
Total	\$275,000.00		

Estimated Completion Date: **Completed**

Phase: **Construction (CON)**


Overall Project Details:

Widen the sections of the road; soft spot repair; asphalt overlay entire road; removed high shoulders, filled in low shoulders; center line and edge line striping; insalled reflective center line markers; paint all stops, stop ahead's and limit bars.

Project Status:

Completed

Add photos/renderings:

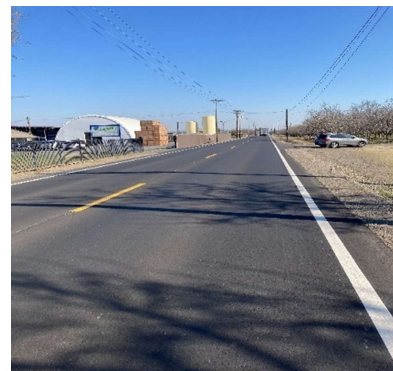



County of Stanislaus
Department of Public Works
1716 Morgan Rd.
Modesto, CA. 95358
Phone (209) 525-4130

Measure L

County Name: **Stanislaus County**

Project Name and Number: Urban Pavement Preservation - Phase F (220017)

Date: 6/30/2026

Revenue		Expenses	
County Funds		Project Budget	\$150,366.87
Federal Funds		Encumbered	
State Funds		Expended - Measure L	\$150,366.87
Measure L Funds BUDGETED	150,366.87	Available - Measure L	\$0.00
Other Funds			
Total	150,366.87		

Estimated Completion Date: Part 1: January 2024 Part 2: December 2024

Phase: Part 1: Complete Part 2: Complete

Overall Project Details:

Pavement treatment/preservation of Industrial Business Parks throughout County.

Project Status:

Part 1: Project has been completed.

Part 2: Project has been completed.

PROJECT 220017; Add photos/renderings:





County of Stanislaus
Department of Public Works
1716 Morgan Rd.
Modesto, CA. 95358
Phone (209) 525-4130

Measure L

County Name: **Stanislaus County**

Project Name and Number: **TRAFFIC SIGNALS (220022)**

Date: **6/30/2026**

Revenue		Expenses	
County Funds		Project Budget	\$150,000.00
Federal Funds		Encumbered	
State Funds		Expended - Measure L	\$49.27
Measure L Funds	\$150,000.00	Available - Measure L	\$149,950.73
Other Funds			
Total	\$150,000.00		

Estimated Completion Date: **Work Complete**

Phase: **Work Complete**

Overall Project Details:

Implement Signal ATMS

Project Status:

Final billing and project close out underway

Add photos/renderings:



County of Stanislaus
Department of Public Works
1716 Morgan Rd.
Modesto, CA. 95358
Phone (209) 525-4130

Measure L

County Name: **Stanislaus County**

Project Name and Number: 2022-2023 Traffic Safety (230008)

Date: 6/30/2026

Revenue		Expenses	
County Funds		Project Budget	\$400,000.00
Federal Funds		Encumbered	
State Funds		Expended - Measure L	\$142,951.64
Measure L Funds	\$400,000.00	Available - Measure L	\$257,048.36
Other Funds/deposits			
Total	\$400,000.00		

Estimated Completion Date: June 30, 2026

Phase: Construction

Overall Project Details:

Analyze and install safety improvements at various locations.

Project Status:

Implementation of traffic safety equipment throughout the county including, but not limited to the following: analyzing traffic safety complaints and purchasing items such as Streetlights, Flashing crosswalk lights, radar feedback signs, Stop Sign installation etc.

Add photos/renderings:



County of Stanislaus
Department of Public Works
1716 Morgan Rd.
Modesto, CA. 95358
Phone (209) 525-4130

Measure L

County Name: **Stanislaus County**

Project Name and Number: **Replace Keyes Rd Bridge ov TID Main Canal (230023)**

Date: **6/30/2026**

Revenue		Expenses	
County Funds		Project Budget	\$2,775,000.00
Federal Funds		Encumbered	
State Funds		Expended - Measure L	\$16,030.49
Measure L Funds	\$50,000.00	Available - Measure L	\$33,969.51
Other Funds-SB1	\$2,725,000.00		
Total	\$2,775,000.00		

Estimated Completion Date: **May 1, 2026**

Phase: **Construction**

Overall Project Details:

Remove and replace a 100+ year old, load-restricted canal crossing located 0.8 miles west of Hickman Road.

Project Status:

Project is complete

Add photos/renderings:





County of Stanislaus
Department of Public Works
1716 Morgan Rd.
Modesto, CA. 95358
Phone (209) 525-4130

Measure L

County Name: **Stanislaus County**

Project Name and Number: Eval @ Repair Slope Failure at Del Puerto Canyon Rd (Parking Area) (230025)

Date: 6/30/2026

Revenue		Expenses	
County Funds		Project Budget	\$50,000.00
Federal Funds		Encumbered	
State Funds		Expended - Measure L	\$72.82
Measure L Funds	\$50,000.00	Available - Measure L	\$49,927.18
Other Funds/deposits			
Total	\$50,000.00		

Estimated Completion Date: Project is no longer active

Phase: Preliminary Engineering (PE)

Overall Project Details:

This Project will repair the existing Del Puerto Canyon Road where the road is currently failing due to the failure of the slope that the road is constructed on.

Project Status:

Project is no longer active

Add photos/renderings:



County of Stanislaus
Department of Public Works
1716 Morgan Rd.
Modesto, CA. 95358
Phone (209) 525-4130

Measure L

County Name: **Stanislaus County**

Project Name and Number: **2023 Sperry Road Repair at I-5 Interchange (230027)**

Date: **6/30/2026**

Revenue		Expenses	
County Funds		Project Budget	\$0.00
Federal Funds		Encumbered	
State Funds		Expended - Measure L	\$11,789.75
Measure L Funds BUDGETED	\$11,789.75	Available - Measure L	\$0.00
Other Funds/deposits			
Total	\$11,789.75		

Estimated Completion Date: **April/May 2024**

Phase: **Complete**

Overall Project Details:

Mill and HMA Overlay of Sperry Ave from west of the Aqueduct to the southbound on/off ramp.

Project Status:

Project is complete

PROJECT 230027; Add photos/renderings:





County of Stanislaus
Department of Public Works
1716 Morgan Rd.
Modesto, CA. 95358
Phone (209) 525-4130

Measure L

County Name: **Stanislaus County**

Project Name and Number: Bridge Preventative Maint - Scour BPMP PM00192 (240011)

Date: 6/30/2026

Revenue		Expenses	
County Funds		Project Budget	\$219,466.00
Federal Funds		Encumbered	
State Funds		Expended - Measure L	\$15,549.75
Measure L Funds	\$54,466.00	Available - Measure L	\$38,916.25
Other Funds/SB1/RMRA	\$165,000.00		
Total	\$219,466.00		

Estimated Completion Date: July 2028

Phase: Preliminary Engineering (PE)

Overall Project Details:

Three bridges within Stanislaus County have been identified as requiring repairs to existing scour countermeasures as part of the BPMP.

Project Status:

The process for removing the Elm Ave bridge from the project scope is ongoing with Caltrans. Environmental and geological studies for the remaining 2 bridges are in progress. Due to the reduction in scope, a revised PES form has been prepared and will be sent to Caltrans for review.

Add photos/renderings:



County of Stanislaus
Department of Public Works
1716 Morgan Rd.
Modesto, CA. 95358
Phone (209) 525-4130

Measure L

County Name: **Stanislaus County**

Project Name and Number: Bridge Preventative Maintenance PM00185 (240012)

Date: 6/30/2026

Revenue		Expenses	
County Funds		Project Budget	\$293,466.29
Federal Funds		Encumbered	
State Funds		Expended - Measure L	\$1,863.49
Measure L Funds	\$1,863.49	Available - Measure L	\$0.00
Other Funds/SB1-RMRA	\$291,602.80		
Total	\$293,466.29		

Estimated Completion Date: Spring 2029

Phase: Preliminary Engineering (PE)

Overall Project Details:

Bridge preventive maintenance at various locations around Stanislaus County. The issues at these bridges include but are not limited to repairing spalled areas, railing repair, joint repair, cleaning rebar, and bridge deck repair.

Project Status:

The Consultant completed their initial 43 bridge inspections in March 2026. The inspection data is currently being analyzed. The Preliminary Environmental Study (PES) Form is nearly complete and will be submitted to Caltrans soon.

Add photos/renderings:



County of Stanislaus
Department of Public Works
1716 Morgan Rd.
Modesto, CA. 95358
Phone (209) 525-4130

Measure L

County Name: Stanislaus County

Project Name and Number: Del Puerto Canyon Road Mile 13 (240014)

Date: 8/8/2025

Revenue		Expenses	
County Funds		Project Budget	\$81,656
Federal Funds		Encumbered	
State Funds		Expended	\$81,656
Measure L Funds	\$81,656	Available	\$0
Other Funds/deposits		Engineering/Roads Labor	
Total	\$81,656	Equipment Charges	

Estimated Completion Date: Summer of 2027

Phase: CE

Overall Project Details:

After winter storms, roadway cracks and vertical settlement were discovered across both lanes of traffic on Del Puerto Canyon Road near PM 13. Preliminary monitoring suggests the road is sitting on a slip plane approximately 40 feet deep. The existing slope will need to be stabilized prior to repairing the existing

Project Status:

The County has received approval of the Damage Assessment Form (DAF) showing the needed additional funding, however, the County is still pending an approval of additional funds from Caltrans.

Add photos/renderings:



County of Stanislaus
Department of Public Works
1716 Morgan Rd.
Modesto, CA. 95358
Phone (209) 525-4130

Measure L

County Name: **Stanislaus County**

Project Name and Number: Urban Pavement preservation (250005)

Date: 6/30/2026

Revenue		Expenses	
County Funds		Project Budget	\$3,153,950.74
Federal Funds		Encumbered	
State Funds		Expended - Measure L	\$3,153,950.74
Measure L Funds	\$3,153,950.74	Available - Measure L	\$0.00
Other Funds/deposits			
Total	\$3,153,950.74		

Estimated Completion Date: Completed

Phase: Closeout

Overall Project Details:

Urban Pavement Preservation Phase H will improve the pavement surface on various roads in West Modesto and Ceres urban County pockets, plus the unincorporated areas of Grayson and Westley. The project will also provide ADA curb ramp upgrades and striping improvements.

Project Status:

Construction is complete. The project will remain open until financial obligations (invoices for work in City of Modesto ROW and CalRecycle Grant payment request) are finalized. The invoice to the City of Modesto has been drafted and will be sent in August 2026. The final report with payment request to CalRecycle is being drafted.

PROJECT 250005; Add photos/renderings:





County of Stanislaus
Department of Public Works
1716 Morgan Rd.
Modesto, CA. 95358
Phone (209) 525-4130

Measure L

County Name: **Stanislaus County**

Project Name and Number: Scour Counter Measure Morgan Road over TID Lateral 5 (250014)

Date: 6/30/2026

Revenue		Expenses	
County Funds		Project Budget	\$444,767.00
Federal Funds		Encumbered	
State Funds		Expended - Measure L	\$2,718.62
Measure L Funds	\$444,767.00	Available - Measure L	\$442,048.38
Other Funds/deposits			
Total	\$444,767.00		

Estimated Completion Date: Spring 2030

Phase: Preliminary Engineering (PE)

Overall Project Details:

Install scour countermeasures at both bridge abutments including wing walls.

Project Status:

Permission to Enter (PTE) agreements have been sent out to property owners for topographic and environmental surveys. The County has received all but one signed PTE. The preliminary environmental work is underway along with the initial design work..

Add photos/renderings:



County of Stanislaus
Department of Public Works
1716 Morgan Rd.
Modesto, CA. 95358
Phone (209) 525-4130

Measure L

County Name: **Stanislaus County**

Project Name and Number: Scour Counter Measure Warnerville Road over Dry Creek 38C0270 (250015)

Date: 6/30/2026

Revenue		Expenses	
County Funds		Project Budget	\$44,459.00
Federal Funds		Encumbered	
State Funds		Expended - Measure L	\$2,392.34
Measure L Funds	\$44,459.00	Available - Measure L	\$42,066.66
Other Funds/deposits			
Total	\$44,459.00		

Estimated Completion Date: Fall 2030

Phase: Preliminary Engineering (PE)

Overall Project Details:

This is a bridge scour mitigation project.

Project Status:

Permission to Enter (PTE) agreements have been sent out to property owners for topographic and environmental surveys. The County has received back all the needed agreements. The preliminary environmental work is underway along with the initial design work.

Add photos/renderings:



County of Stanislaus
Department of Public Works
1716 Morgan Rd.
Modesto, CA. 95358
Phone (209) 525-4130

Measure L

County Name: **Stanislaus County**

Project Name and Number: Scour Counter Measure Willms Road over Dry Creek (250016)

Date: 6/30/2026

Revenue		Expenses	
County Funds		Project Budget	\$44,525.00
Federal Funds		Encumbered	
State Funds		Expended - Measure L	\$2,363.43
Measure L Funds	\$44,525.00	Available - Measure L	\$42,161.57
Other Funds/deposits			
Total	\$44,525.00		

Estimated Completion Date: Fall 2030

Phase: Preliminary Engineering (PE)

Overall Project Details:

This is a bridge scour mitigation project.

Project Status:

Permission to Enter (PTE) agreements have been sent out to property owners for topographic and environmental surveys. The County has received back all the needed agreements. The preliminary environmental work is underway along with the initial design work

Add photos/renderings:



County of Stanislaus
Department of Public Works
1716 Morgan Rd.
Modesto, CA. 95358
Phone (209) 525-4130

Measure L

County Name: **Stanislaus County**

Project Name and Number: **Scour Counter Measure Warnerville Road over Dry Creek 38C0307 (250017)**

Date: **6/30/2026**

Revenue		Expenses	
County Funds		Project Budget	\$44,525.00
Federal Funds		Encumbered	
State Funds		Expended - Measure L	\$2,420.74
Measure L Funds	\$44,525.00	Available - Measure L	\$42,104.26
Other Funds/deposits			
Total	\$44,525.00		

Estimated Completion Date: **Fall 2030**

Phase: **Preliminary Engineering (PE)**

Overall Project Details:

Install scour countermeasures at both bridge abutments including wing walls.

Project Status:

Permission to Enter (PTE) agreements have been sent out to property owners for topographic and environmental surveys. The County has received back all the needed agreements. The preliminary environmental work is underway along with the initial design work.

Add photos/renderings:



County of Stanislaus
Department of Public Works
1716 Morgan Rd.
Modesto, CA. 95358
Phone (209) 525-4130

Measure L

County Name: **Stanislaus County**

Project Name and Number: Del Puerto Monitoring 1 and 2 (250018)

Date: 6/30/2026

Revenue		Expenses	
County Funds		Project Budget	\$75,700.00
Federal Funds		Encumbered	
State Funds		Expended - Measure L	\$66,519.34
Measure L Funds	\$75,700.00	Available - Measure L	\$9,180.66
Other Funds/deposits			
Total	\$75,700.00		

Estimated Completion Date: September 2026

Phase: N/A

Overall Project Details:

Install two inclinometers and monitor slope movement at two locations along Del Puerto Canyon Road.

Project Status:

Engeo provided the last set of readings to the County. Engeo will provide a report summarizing the results of all the monitoring data prior to the contract expiring in September 2026.

Add photos/renderings:



County of Stanislaus
Department of Public Works
1716 Morgan Rd.
Modesto, CA. 95358
Phone (209) 525-4130

Measure L

County Name: **Stanislaus County**

Project Name and Number: 2025 Annual Chip (250019)

Date: 6/30/2026

Revenue		Expenses	
County Funds		Project Budget	\$3,000,000.00
Federal Funds		Encumbered	
State Funds		Expended - Measure L	\$1,063,308.90
Measure L Funds	\$3,000,000.00	Available - Measure L	\$1,936,691.10
Other Funds/deposits			
Total	\$3,000,000.00		

Estimated Completion Date: Completed

Phase: Construction (CON)

Overall Project Details:

2025 Chip Seal project is part of the County's Maintenance Program. The Roads division will Chip 116 miles of County roads during this project.

Project Status:

Crews have completed the chip seal and shoulder portion of the project. Currently they are working on the striping and legends.

Add photos/renderings:



County of Stanislaus
Department of Public Works
1716 Morgan Rd.
Modesto, CA. 95358
Phone (209) 525-4130

Measure L

County Name: Stanislaus County

Project Name and Number: Morgan EV Charging Station (250020)

Date: 8/14/2025

Revenue		Expenses	
County Funds		Project Budget	\$1,439.08
Federal Funds		Encumbered	
State Funds		Expended	\$1,439.08
Measure L Funds	\$1,439.08	Available	\$0.00
Other Funds/deposits		Engineering/Roads Labor	
Total	\$1,439.08	Equipment Charges	

Estimated Completion Date: 9/30/2027

Phase: Other

Overall Project Details:

Improve alternative fuel facilities, acquire EV equipment, and purchase two electric vehicles.

Project Status:

In the process of completing NEPA on this project.

Add photos/renderings:



County of Stanislaus
Department of Public Works
1716 Morgan Rd.
Modesto, CA. 95358
Phone (209) 525-4130

Measure L

County Name: **Stanislaus County**

Project Name and Number: Witmore Paving (250022)

Date: 6/30/2026

Revenue		Expenses	
County Funds		Project Budget	\$300,000.00
Federal Funds		Encumbered	
State Funds		Expended - Measure L	\$147.24
Measure L Funds	\$300,000.00	Available - Measure L	\$299,852.76
Other Funds/deposits			
Total	\$300,000.00		

Estimated Completion Date: Summer 2026

Phase: Preliminary Engineering (PE)

Overall Project Details:

Pavement replacement project on Whitmore between Morgan and Crows Landing Road.

Project Status:

In design, the County is finalizing an MOU with the City of Ceres.

Add photos/renderings:



County of Stanislaus
Department of Public Works
1716 Morgan Rd.
Modesto, CA. 95358
Phone (209) 525-4130

Measure L

County Name: **Stanislaus County**

Project Name and Number: Urban Pavement Preservation - Phase I (250024)

Date: 6/30/2026

Revenue		Expenses	
County Funds		Project Budget	\$3,500,000.00
Federal Funds		Encumbered	
State Funds		Expended - Measure L	\$135,945.54
Measure L Funds	\$3,500,000.00	Available - Measure L	\$3,364,054.46
Other Funds/deposits			
Total	\$3,500,000.00		

Estimated Completion Date: Nov-26

Phase: Pre-Construction

Overall Project Details:

The project will treat various roads in north Salida and Modesto. It will provide pavement preservation treatments such as microsurfacing, asphalt-rubber chip seal, and slurry seal, plus new striping, digouts, and crack treatment.

Project Status:

The project was advertised and bid in June. Construction is set to begin after BOS approval at the end of August.

Add photos/renderings:



County of Stanislaus
Department of Public Works
1716 Morgan Rd.
Modesto, CA. 95358
Phone (209) 525-4130

Measure L

County Name: **Stanislaus County**

Project Name and Number: Faith Home Rd. Expressway (260001)

Date: 6/30/2026

Revenue		Expenses	
County Funds		Project Budget	\$1,500,000.00
Federal Funds		Encumbered	
State Funds		Expended - Measure L	\$42,049.39
Measure L Funds	\$1,500,000.00	Available - Measure L	\$1,457,950.61
Other Funds/deposits			
Total	\$1,500,000.00		

Estimated Completion Date: Summer 2029

Phase: PE

Overall Project Details:

The Faith Home Expressway Project will construct a one-mile, two-lane expressway from the existing Faith Home Road and East Hatch Road intersection north to the Garner Road and Finch Road intersection. The current phase will complete 65% plans, specifications, and estimate as well as explore grant opportunities for construction funding.

Project Status:

The project has been kicked off with the County's consultant team. The County and the Consultants are working on obtaining the needed Permission to Enter (PTE) agreements for the project. The team is also working on any preliminary design that can be completed in the absence of the signed PTE agreements.

Add photos/renderings:



County of Stanislaus
Department of Public Works
1716 Morgan Rd.
Modesto, CA. 95358
Phone (209) 525-4130

Measure L

County Name: **Stanislaus County**

Project Name and Number: 2026 Chip Seal (260006)

Date: 6/30/2026

Revenue		Expenses	
County Funds		Project Budget	\$3,000,000.00
Federal Funds		Encumbered	
State Funds		Expended - Measure L	\$1,533,294.10
Measure L Funds	\$3,000,000.00	Available - Measure L	\$1,466,705.90
Other Funds/deposits			
Total	\$3,000,000.00		

Estimated Completion Date: 9/30/2026

Phase: Prep Phase which began March 7th and continuing

Overall Project Details:

2026 Chip Seal project is part of the County's Maintenance Program. The Roads division will Chip 106 miles of County roads during this project.

Project Status:

The crews have begun to stockpile chip and continue with patching, tree clearance, and tabbing in preparation of Chip Phase which will begin August 17th

Add photos/renderings:



County of Stanislaus
Department of Public Works
1716 Morgan Rd.
Modesto, CA. 95358
Phone (209) 525-4130

Measure L

County Name: **Stanislaus County**

Project Name and Number: **Traffic Counts (260008)**

Date: **6/30/2026**

Revenue		Expenses	
County Funds		Project Budget	\$75,000.00
Federal Funds		Encumbered	
State Funds		Expended - Measure L	\$67,003.08
Measure L Funds	\$75,000.00	Available - Measure L	\$7,996.92
Other Funds/deposits			
Total	\$75,000.00		

Estimated Completion Date: **6/30/2026**

Phase: **Closeout**

Overall Project Details:

Review and implement traffic counts program.

Project Status:

Final billing and project close out underway.

Add photos/renderings:



County of Stanislaus
Department of Public Works
1716 Morgan Rd.
Modesto, CA. 95358
Phone (209) 525-4130

Measure L

County Name: **Stanislaus County**

Project Name and Number: **Claus Rd, Santa Fe Ave & Terminal Ave Intersecation(260010)**

Date: **6/30/2026**

Revenue		Expenses	
County Funds		Project Budget	\$25,000.00
Federal Funds		Encumbered	
State Funds		Expended - Measure L	\$17,766.03
Measure L Funds	\$25,000.00	Available - Measure L	\$7,233.97
Other Funds/deposits			
Total	\$25,000.00		

Estimated Completion Date: **TBD pending additional local funding for design and construction**

Phase: **Preliminary Engineering (PE)**

Overall Project Details:

Realign the intersection of Claus Road and Terminal Avenue/Santa Fe Avenue and improve drainage.

Project Status:

Project currently only has funding for the topographic survey of the intersection. The survey field work has been completed. County staff is currently analyzing and drafting the survey data. Future design and construction are pending additional local funding.

Add photos/renderings:



County of Stanislaus
Department of Public Works
1716 Morgan Rd.
Modesto, CA. 95358
Phone (209) 525-4130

Measure L

County Name: **Stanislaus County**

Project Name and Number: **Fonroche Lighting America - Solar Street Lights (3 locations) (260016)**

Date: **3/31/2026**

Revenue		Expenses	
County Funds		Project Budget	\$51,000.00
Federal Funds		Encumbered	
State Funds		Expended - Measure L	\$11,198.25
Measure L Funds	\$51,000.00	Available - Measure L	\$39,801.75
Other Funds/deposits			
Total	\$51,000.00		

Estimated Completion Date: **6/30/2026**

Phase: **CON**

Overall Project Details:

Install solar street lights

Project Status:

Purchase and install solar street lights along Kerr Bike Trail and Ripon/Hammet Bike trail where existing street lights have been vandalized or malfunctioning. This project will also install a new solar street light and flashing warning lights at Broadway Ave and Curtis Rd in Salida for pedestrian safety.

Add photos/renderings:
